

# Delayed and Reopen Ticket Report

Generated: 02 July 2026 08:06 | Project: IAMS30 | Board: IAMS 3.0

Report ini membandingkan waktu ticket berstatus **In Progress** saat ini dengan rata-rata historis waktu pengerjaan **To Do** → **DEV DONE** (5 sprint terakhir per tim) untuk Story Point yang sama. Ticket dianggap **delayed** jika sudah In Progress lebih lama dari rata-rata tersebut.

## Baseline Rata-rata (To Do -> DEV DONE)

| Story Point | MKP Team (hari) | BUMA ID Team (hari) |
|-------------|-----------------|---------------------|
| 1           | 1.78            | 1.09                |
| 2           | 5.45            | 2.36                |
| 3           | 5.22            | 8.25                |
| 5           | 9.79            | 9.76                |
| 8           | 15.06           | 21.63               |

## S2 IAMS — BUMA ID Team

Total ticket In Progress: 9 | Delayed: 3 | On Track: 3 | No Baseline (SP di luar 1/2/3/5/8): 3

### Delayed Tickets

| Key         | Summary                                                                    | Assignee    | SP | Started    | Sprint Start | Elapsed (hari) | Baseline (hari) | Delay (hari) | Priority |
|-------------|----------------------------------------------------------------------------|-------------|----|------------|--------------|----------------|-----------------|--------------|----------|
| IAMS30-4270 | [FE] Form Bundle — Choose Form: Step 2 Stepper in Create Plan Modal de...  | dimas.wahyu | 2  | 2026-06-26 | 2026-06-25   | 3.7            | 2.4             | 1.3          | Medium   |
| IAMS30-4271 | [FE] Form Bundle — Fetch Form List on Enter Step 2 (Choose Form)           | dimas.wahyu | 2  | 2026-06-26 | 2026-06-25   | 3.4            | 2.4             | 1.1          | Medium   |
| IAMS30-4272 | [FE] Form Package — Extend Create Plan: Include Forms Array in Request ... | dimas.wahyu | 2  | 2026-06-29 | 2026-06-25   | 2.5            | 2.4             | 0.1          | Medium   |

On Track Tickets

| Key         | Summary                                                                   | Assignee           | SP | Started    | Elapsed (hari) | Baseline (hari) | Priority |
|-------------|---------------------------------------------------------------------------|--------------------|----|------------|----------------|-----------------|----------|
| IAMS30-4266 | [BE] Form Package — Plan Submit: Outbox Pattern + PlanSubmitted Event ... | Riki Ahmad Fadilah | 3  | 2026-06-29 | 2.6            | 8.2             | Medium   |

| Key         | Summary                                                                   | Assignee       | SP | Started    | Elapsed (hari) | Baseline (hari) | Priority |
|-------------|---------------------------------------------------------------------------|----------------|----|------------|----------------|-----------------|----------|
| IAMS30-4273 | [MOBILE] Form Package — Tab Form: Form List, Summary Bar, Status, and ... | nurrahman hadi | 5  | 2026-06-29 | 2.5            | 9.8             | Medium   |
| IAMS30-4274 | [MOBILE] Form Package — Tap Form Card: Render Form from Cosmos Snapsho... | nurrahman hadi | 5  | 2026-06-29 | 2.5            | 9.8             | Medium   |

### No Baseline (SP tidak termasuk 1/2/3/5/8)

| Key         | Summary                                                                    | Assignee           | SP | Started    | Elapsed (hari) | Priority |
|-------------|----------------------------------------------------------------------------|--------------------|----|------------|----------------|----------|
| IAMS30-4245 | Bug - [Mobile] Field Unit Serial Number tidak berfungsi di form submission | dimas.wahyu        | -  | 2026-06-25 | 4.8            | High     |
| IAMS30-4284 | Bug - [Mobile] PM Shutdown Component List Tidak Lengkap                    | nurrahman hadi     | -  | 2026-06-25 | 4.7            | High     |
| IAMS30-4388 | Bug - [Web] Order Approval - Approval Unit2 IPR ini masuk ke approver ADT  | Riki Ahmad Fadilah | -  | 2026-06-29 | 2.5            | Medium   |

### Reopened Tickets

| Key         | Summary                                                         | Status  | Assignee     | Reopen Count | Priority | New Today |
|-------------|-----------------------------------------------------------------|---------|--------------|--------------|----------|-----------|
| IAMS30-4075 | [BE] Inspection Monitoring - Generate Multi-Assignee PDF Report | Re-open | Dian Heryana | 1            | Highest  |           |

## Current Progress Sprint

| Metric                           | Tickets                                  | Story Points                             |
|----------------------------------|------------------------------------------|------------------------------------------|
| Total                            | 42                                       | 62 SP                                    |
| Done / QA Passed                 | 13 (31%)                                 | 12 SP (19%)                              |
| In Progress / Dev Done / QA Test | 18                                       | 30 SP                                    |
| To Do                            | 11                                       | 20 SP                                    |
| <b>Progress (Tickets / SP)</b>   | <div> <div></div> <div></div> </div> 31% | <div> <div></div> <div></div> </div> 19% |
| <b>Sprint Day Progress</b>       | 6 / 10 hari kerja                        | <div> <div></div> <div></div> </div> 60% |

## To Do Tickets

| Key         | Summary                                                                   | Status | Assignee           | SP | Priority |
|-------------|---------------------------------------------------------------------------|--------|--------------------|----|----------|
| IAMS30-4053 | [AutoCreate] Refinement auto create Plan for Unschedule Breakdown         | To Do  | Unassigned         | 3  | Medium   |
| IAMS30-4189 | [BE] Generate PDF for General Form Submission                             | To Do  | Dian Heryana       | 3  | Medium   |
| IAMS30-4281 | [BE] SiteShift — Extend Offline Sync: Include SiteShift Data for Mobil... | To Do  | Riki Ahmad Fadilah | 3  | Medium   |

...dan 8 ticket lainnya — lihat backlog di board.

## Migration Digiplan - S8 — MKP Team

Total ticket In Progress: **5** | Delayed: **0** | On Track: **5** | No Baseline (SP di luar 1/2/3/5/8): **0**

### ● Delayed Tickets

Selamat, tidak ada ticket yang delayed hari ini.

### ● On Track Tickets

| Key         | Summary                                                    | Assignee         | SP | Started    | Elapsed (hari) | Baseline (hari) | Priority |
|-------------|------------------------------------------------------------|------------------|----|------------|----------------|-----------------|----------|
| IAMS30-4389 | [BE] Stock and Part — Get List Material API                | v-darwin.sam alo | 3  | 2026-06-30 | 1.5            | 5.2             | Medium   |
| IAMS30-4392 | [FE] Stock and Part — Flag Tab Page (MaterialR anking)     | Yvonne Priscilla | 2  | 2026-06-30 | 1.7            | 5.4             | Medium   |
| IAMS30-4391 | [BE] Stock and Part — Flag Tab CRUD API (MaterialR anking) | v-darwin.sam alo | 3  | 2026-07-01 | 0.7            | 5.2             | Medium   |

...dan 2 ticket lainnya — lihat backlog di board.

### 🔄 Reopened Tickets

Nihil! Gak ada ticket yang bolak-balik reopen — sekali jadi langsung mantap. 🙌

### 📊 Current Progress Sprint

| Metric                           | Tickets  | Story Points |
|----------------------------------|----------|--------------|
| Total                            | 44       | 115 SP       |
| Done / QA Passed                 | 17 (39%) | 36 SP (31%)  |
| In Progress / Dev Done / QA Test | 17       | 54 SP        |

| Metric                  | Tickets                    | Story Points               |
|-------------------------|----------------------------|----------------------------|
| To Do                   | 10                         | 25 SP                      |
| Progress (Tickets / SP) | <div><div></div></div> 39% | <div><div></div></div> 31% |
| Sprint Day Progress     | 4 / 10 hari kerja          | <div><div></div></div> 40% |

## To Do Tickets

| Key         | Summary                                                                   | Status | Assignee              | SP | Priority |
|-------------|---------------------------------------------------------------------------|--------|-----------------------|----|----------|
| IAMS30-4079 | [MKP2] Re-implement Section CRUD using dedicated Section table (User D... | To Do  | Sarayevi Zalanderi    | 5  | Medium   |
| IAMS30-4216 | [MKP2] Parameterisasi business logic filter SP backlog monitoring untu... | To Do  | Varian Aditya Iryanto | 5  | Medium   |
| IAMS30-4393 | [BE] Order Type — CRUD API (MaterialCostType)                             | To Do  | Sarayevi Zalanderi    | 3  | Medium   |

...dan 7 ticket lainnya — lihat backlog di board.


## Insight: Velocity Trend — Rata-rata Cycle Time per Sprint (5 Sprint Terakhir)

Rata-rata waktu penyelesaian (To Do -> DEV DONE) dalam hari, dihitung per sprint untuk 5 sprint closed terakhir masing-masing tim, dipecah per Story Point. S1 = sprint tertua, S5 = sprint terbaru.


| #  | MKP Team Sprint         | BUMA ID Team Sprint      |
|----|-------------------------|--------------------------|
| S1 | Migrating Digiplan - S3 | Release 3.1.0 (Sprint 2) |
| S2 | Migration Digiplan - S4 | Release 4.0.0 - S1       |
| S3 | Migration Digiplan - S5 | Release 4.0.0 - S2       |
| S4 | Migration Digiplan - S6 | Release 4.0.0 - S3       |

| #  | MKP Team Sprint         | BUMA ID Team Sprint     |
|----|-------------------------|-------------------------|
| S5 | Migration Digiplan - S7 | 4.1.0 - Improve and Fix |


### Story Point 1




### Story Point 2




### Story Point 3



### Story Point 5



### Story Point 8

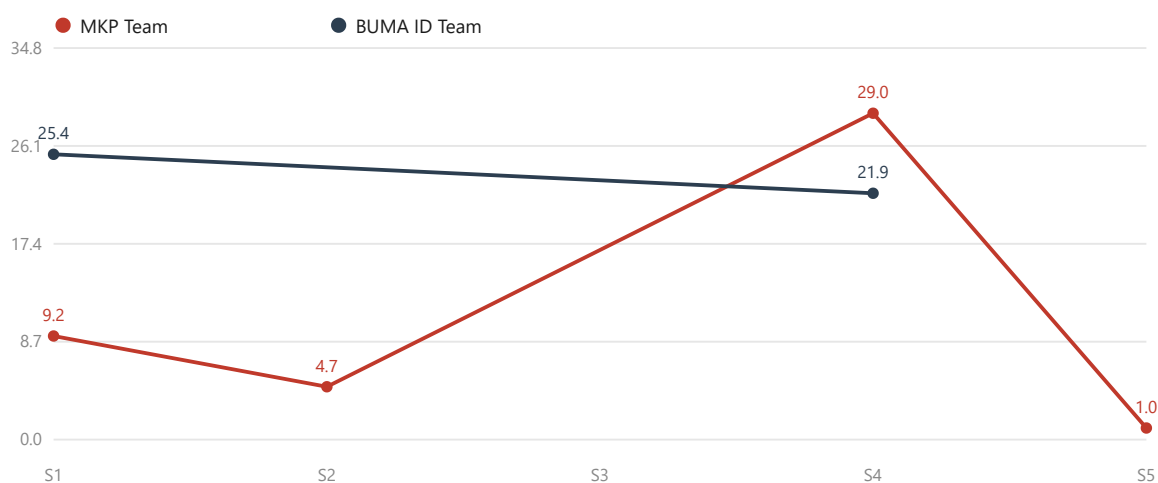

### Velocity per Orang — 5 Sprint Terakhir

SP dihitung dari ticket utama (parent). Setiap orang yang terlibat (assignee ticket utama maupun sub-ticket) mendapatkan SP penuh dari ticket tersebut.

## MKP Team

| #  | Sprint                  |
|----|-------------------------|
| S1 | Migrating Digiplan - S3 |
| S2 | Migration Digiplan - S4 |
| S3 | Migration Digiplan - S5 |
| S4 | Migration Digiplan - S6 |
| S5 | Migration Digiplan - S7 |

| Nama                     | S1 | S2 | S3 | S4 | S5 |
|--------------------------|----|----|----|----|----|
| Darwin Samalo            | 42 | 54 | 53 | 42 | 28 |
| Yvonne Priscilla         | 26 | 28 | 20 | 50 | 29 |
| Sarayevi<br>Zalanderi    | 16 | 5  | 8  | 27 | 18 |
| Varian Aditya<br>Iryanto | 5  | 8  | 14 | 12 | 4  |
| Herianto Salim           | 5  | -  | 6  | 6  | 5  |
| Andrian<br>Sebayang      | 24 | 46 | 60 | 62 | 50 |
| Muhammad Zul<br>Fikar    | 44 | 30 | 24 | 41 | 26 |
| Gita Riskayanti          | 10 | 7  | 5  | 22 | 11 |

## BUMA ID Team

| #  | Sprint                   |
|----|--------------------------|
| S1 | Release 3.1.0 (Sprint 2) |
| S2 | Release 4.0.0 - S1       |
| S3 | Release 4.0.0 - S2       |
| S4 | Release 4.0.0 - S3       |
| S5 | 4.1.0 - Improve and Fix  |

| Nama              | S1 | S2 | S3 | S4 | S5 |
|-------------------|----|----|----|----|----|
| Dimas Wahyu P     | 19 | 5  | 18 | 26 | 14 |
| Dian Heryana      | 32 | 13 | 31 | 26 | 25 |
| Nurrahman<br>Hadi | 32 | 14 | 27 | 35 | 19 |



| Nama            | S1 | S2 | S3 | S4 | S5 |
|-----------------|----|----|----|----|----|
| Riki Ahmad F    | 36 | 26 | 33 | 48 | 23 |
| Gita Riskayanti | 32 | 23 | 39 | 23 | 38 |
| Muhammad Zaqi   | 45 | 30 | 31 | 43 | 38 |
