

Delayed and Reopen Ticket Report

Generated: 03 July 2026 08:58 | Project: IAMS30 | Board: IAMS 3.0

Report ini membandingkan waktu ticket berstatus **In Progress** saat ini dengan rata-rata historis waktu pengerjaan **To Do** → **DEV DONE** (5 sprint terakhir per tim) untuk Story Point yang sama. Ticket dianggap **delayed** jika sudah In Progress lebih lama dari rata-rata tersebut.

Baseline Rata-rata (To Do -> DEV DONE)

Story Point	MKP Team (hari)	BUMA ID Team (hari)
1	1.78	1.09
2	5.45	2.36
3	5.22	8.25
5	9.79	9.76
8	15.06	21.63

S2 IAMS — BUMA ID Team

Total ticket In Progress: 8 | Delayed: 2 | On Track: 3 | No Baseline (SP di luar 1/2/3/5/8): 3

● Delayed Tickets

Key	Summary	Assignee	SP	Started	Sprint Start	Elapsed (hari)	Baseline (hari)	Delay (hari)	Priority
IAMS30-4267	[BE] Form Package — Extend Get Work Card Detail (Online): Include Pack...	Dian Heryana	2	2026-06-29	2026-06-25	3.7	2.4	1.3	Medium
IAMS30-4268	[BE] Form Package — Extend Get Work Card Detail (Offline Mode): Includ...	Dian Heryana	2	2026-06-29	2026-06-25	3.7	2.4	1.3	Medium

● On Track Tickets

Key	Summary	Assignee	SP	Started	Elapsed (hari)	Baseline (hari)	Priority
IAMS30-4266	[BE] Form Package — Plan Submit: Outbox Pattern + PlanSubmitted Event ...	Riki Ahmad Fadilah	3	2026-06-29	3.7	8.2	Medium
IAMS30-4273	[MOBILE] Form Package — Tab Form: Form List, Summary Bar, Status, and ...	nurrahman hadi	5	2026-06-29	3.5	9.8	Medium

Key	Summary	Assignee	SP	Started	Elapsed (hari)	Baseline (hari)	Priority
IAMS30-4274	[MOBILE] Form Package — Tap Form Card: Render Form from Cosmos Snapsho...	nurrahman hadi	5	2026-06-29	3.5	9.8	Medium

No Baseline (SP tidak termasuk 1/2/3/5/8)

Key	Summary	Assignee	SP	Started	Elapsed (hari)	Priority
IAMS30-4245	Bug - [Mobile] Field Unit Serial Number tidak berfungsi di form submission	dimas.wahyu	-	2026-06-25	5.9	High
IAMS30-4284	Bug - [Mobile] PM Shutdown Component List Tidak Lengkap	nurrahman hadi	-	2026-06-25	5.8	High
IAMS30-4388	Bug - [Web] Order Approval - Approval Unit2 IPR ini masuk ke approver ADT	Riki Ahmad Fadilah	-	2026-06-29	3.5	Medium

Reopened Tickets

Key	Summary	Status	Assignee	Reopen Count	Priority	New Today
IAMS30-4075	[BE] Inspection Monitoring - Generate Multi-Assignee PDF Report	QA TEST	Dian Heryana	1	Highest	

Key	Summary	Status	Assignee	Reopen Count	Priority	New Today
IAMS30-4265	[BE] Form Package — Get Form List by Equipment Model and Service Type	Re-open	Riki Ahmad Fadilah	1	Medium	

Current Progress Sprint

Metric	Tickets	Story Points
Total	42	62 SP
Done / QA Passed	19 (45%)	18 SP (29%)
In Progress / Dev Done / QA Test	14	28 SP
To Do	9	16 SP
Progress (Tickets / SP)	45%	29%
Sprint Day Progress	7 / 10 hari kerja	70%

To Do Tickets

Key	Summary	Status	Assignee	SP	Priority
IAMS30-4053	[AutoCreate] Refinement auto create Plan for Unschedule Breakdown	To Do	Unassigned	3	Medium
IAMS30-4189	[BE] Generate PDF for General Form Submission	To Do	Dian Heryana	3	Medium
IAMS30-4281	[BE] SiteShift — Extend Offline Sync: Include SiteShift Data for Mobil...	To Do	Riki Ahmad Fadilah	3	Medium

...dan 6 ticket lainnya — lihat backlog di board.

Migration Digiplan - S8 — MKP Team

Total ticket In Progress: **4** | Delayed: **0** | On Track: **4** | No Baseline (SP di luar 1/2/3/5/8): **0**

● Delayed Tickets

Selamat, tidak ada ticket yang delayed hari ini.

● On Track Tickets

Key	Summary	Assignee	SP	Started	Elapsed (hari)	Baseline (hari)	Priority
IAMS30-4390	[FE] Stock and Part — List Tab Page	Yvonne Priscilla	1	2026-07-02	0.7	1.8	Medium
IAMS30-4389	[BE] Stock and Part — Get List Material API	v-darwin.samalo	3	2026-06-30	2.6	5.2	Medium
IAMS30-4392	[FE] Stock and Part — Flag Tab Page (MaterialRanking)	Yvonne Priscilla	2	2026-06-30	2.7	5.4	Medium

...dan 1 ticket lainnya — lihat backlog di board.

🔄 Reopened Tickets

Nihil! Gak ada ticket yang bolak-balik reopen — sekali jadi langsung mantap. 🙌

📊 Current Progress Sprint

Metric	Tickets	Story Points
Total	44	115 SP
Done / QA Passed	18 (41%)	37 SP (32%)
In Progress / Dev Done / QA Test	17	54 SP
To Do	9	24 SP

Metric	Tickets	Story Points
Progress (Tickets / SP)	41%	32%
Sprint Day Progress	5 / 10 hari kerja	50%

To Do Tickets

Key	Summary	Status	Assignee	SP	Priority
IAMS30-4079	[MKP2] Re-implement Section CRUD using dedicated Section table (User D...	To Do	Sarayevi Zalanderi	5	Medium
IAMS30-4216	[MKP2] Parameterisasi business logic filter SP backlog monitoring untu...	To Do	Varian Aditya Iryanto	5	Medium
IAMS30-4393	[BE] Order Type — CRUD API (MaterialCostType)	To Do	Sarayevi Zalanderi	3	Medium


...dan 6 ticket lainnya — lihat backlog di board.

Insight: Velocity Trend — Rata-rata Cycle Time per Sprint (5 Sprint Terakhir)


Rata-rata waktu penyelesaian (To Do -> DEV DONE) dalam hari, dihitung per sprint untuk 5 sprint closed terakhir masing-masing tim, dipecah per Story Point. S1 = sprint tertua, S5 = sprint terbaru.

#	MKP Team Sprint	BUMA ID Team Sprint
S1	Migrating Digiplan - S3	Release 3.1.0 (Sprint 2)
S2	Migration Digiplan - S4	Release 4.0.0 - S1
S3	Migration Digiplan - S5	Release 4.0.0 - S2
S4	Migration Digiplan - S6	Release 4.0.0 - S3
S5	Migration Digiplan - S7	4.1.0 - Improve and Fix


Story Point 1




Story Point 2




Story Point 3



Story Point 5



Story Point 8

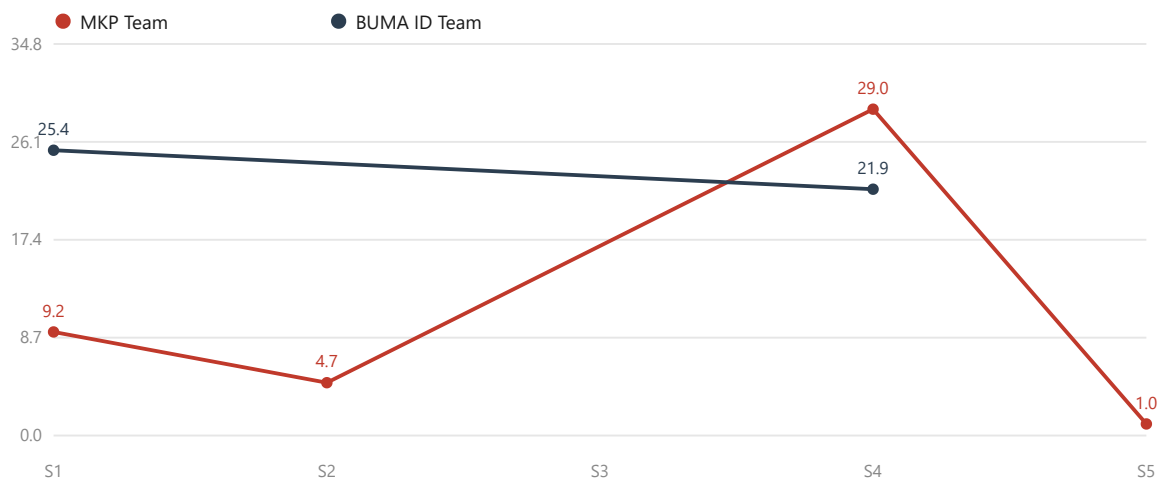

Velocity per Orang — 5 Sprint Terakhir

SP dihitung dari ticket utama (parent). Setiap orang yang terlibat (assignee ticket utama maupun sub-ticket) mendapatkan SP penuh dari ticket tersebut.

MKP Team

#	Sprint
S1	Migrating Digiplan - S3
S2	Migration Digiplan - S4
S3	Migration Digiplan - S5
S4	Migration Digiplan - S6
S5	Migration Digiplan - S7

Nama	S1	S2	S3	S4	S5
Darwin Samalo	42	54	53	42	28
Yvonne Priscilla	26	28	20	50	29
Sarayevi Zalanderi	16	5	8	27	18
Varian Aditya Iryanto	5	8	14	12	4
Herianto Salim	5	-	6	6	5
Andrian Sebayang	24	46	60	62	50
Muhammad Zul Fikar	44	30	24	41	26
Gita Riskayanti	10	7	5	22	11

BUMA ID Team

#	Sprint
S1	Release 3.1.0 (Sprint 2)
S2	Release 4.0.0 - S1
S3	Release 4.0.0 - S2
S4	Release 4.0.0 - S3
S5	4.1.0 - Improve and Fix

Nama	S1	S2	S3	S4	S5
Dimas Wahyu P	19	5	18	26	14
Dian Heryana	32	13	31	26	27
Nurrahman Hadi	32	14	27	35	19
Riki Ahmad F	36	26	33	48	23
Gita Riskayanti	32	23	39	23	38

Nama	S1	S2	S3	S4	S5
Muhammad Zaqi	45	30	31	43	40
