

Delayed and Reopen Ticket Report

Generated: 24 June 2026 14:40 | Project: IAMS30 | Board: IAMS 3.0

Report ini membandingkan waktu ticket berstatus **In Progress** saat ini dengan rata-rata historis waktu pengerjaan **To Do** → **DEV DONE** (5 sprint terakhir per tim) untuk Story Point yang sama. Ticket dianggap **delayed** jika sudah In Progress lebih lama dari rata-rata tersebut.

Baseline Rata-rata (To Do -> DEV DONE)

Story Point	MKP Team (hari)	BUMA ID Team (hari)
1	2.18	1.09
2	6.37	2.42
3	6.63	7.56
5	9.44	9.76
8	15.89	21.63

Migration Digiplan - S7 — MKP Team

Total ticket In Progress: **4** | Delayed: **0** | On Track: **4** | No Baseline (SP di luar 1/2/3/5/8): **0**

● Delayed Tickets

Selamat, tidak ada ticket yang delayed hari ini.

● On Track Tickets

Key	Summary	Assignee	SP	Started	Elapsed (hari)	Baseline (hari)	Priority
IAMS30-4143	[FE] Damage — List, Add & Edit Page	Sarayevi Zalanderi	1	2026-06-24	0.0	2.2	Medium

Key	Summary	Assignee	SP	Started	Elapsed (hari)	Baseline (hari)	Priority
IAMS30-4144	[BE] Damage — List, Create, Update API	Sarayevi Zalanderi	3	2026-06-24	0.0	6.6	Medium
IAMS30-4055	Mobile Waterfall Sync Log Monitoring	Muhamma d Abdu Ar Rahman	3	2026-06-24	0.0	6.6	Medium

...dan 1 ticket lainnya — lihat backlog di board.

 Reopened Tickets

Nihil! Gak ada ticket yang bolak-balik reopen — sekali jadi langsung mantap. 🙌

 Current Progress Sprint

Metric	Tickets	Story Points
Total	37	79 SP
Done / QA Passed	20 (54%)	36 SP (46%)
In Progress / Dev Done / QA Test	17	43 SP
To Do	0	0 SP
Progress (Tickets / SP)	54%	46%
Sprint Day Progress	8 / 10 hari kerja	80%

 To Do Tickets


To Do list-nya kosong melompong. Semua udah jalan duluan, gas terus! 🚀

 Insight: Velocity Trend — Rata-rata Cycle Time per Sprint (5 Sprint Terakhir)


Rata-rata waktu penyelesaian (To Do -> DEV DONE) dalam hari, dihitung per sprint untuk 5 sprint closed terakhir masing-masing tim, dipecah per Story Point. S1 = sprint tertua, S5 = sprint terbaru.

#	MKP Team Sprint	BUMA ID Team Sprint
S1	Migrating Digiplan - S2	Release 3.1.0 (Sprint 2)
S2	Migrating Digiplan - S3	Release 4.0.0 - S1
S3	Migration Digiplan - S4	Release 4.0.0 - S2
S4	Migration Digiplan - S5	Release 4.0.0 - S3
S5	Migration Digiplan - S6	4.1.0 - Improve and Fix


Story Point 1




Story Point 2




Story Point 3



Story Point 5



Story Point 8

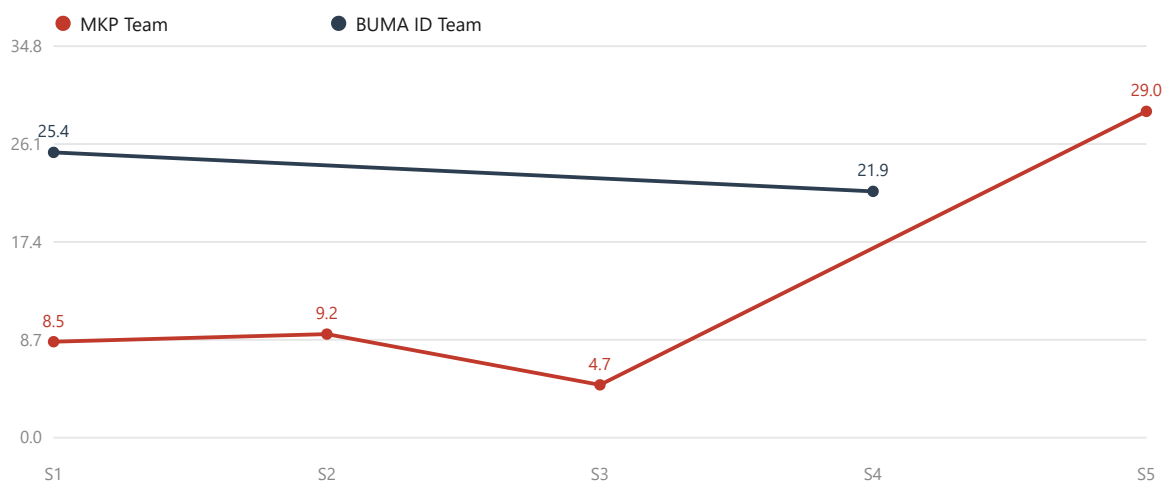



Velocity per Orang — 5 Sprint Terakhir

SP dihitung dari ticket utama (parent). Setiap orang yang terlibat (assignee ticket utama maupun sub-ticket) mendapatkan SP penuh dari ticket tersebut.

MKP Team

#	Sprint
S1	Migrating Digiplan - S2
S2	Migrating Digiplan - S3
S3	Migration Digiplan - S4
S4	Migration Digiplan - S5
S5	Migration Digiplan - S6

Nama	S1	S2	S3	S4	S5	Total
v-darwin.samalo	30	42	54	53	42	221
Yvonne Priscilla	38	26	28	20	50	162
Andrian Sebayang	-	24	24	24	-	72
Sarayevi Zalanderi	13	16	5	8	27	69
nurrahman hadi	5	21	21	16	-	63
Varian Aditya Iryanto	-	5	8	14	12	39
Riki Ahmad Fadilah	-	8	10	8	-	26
Rudy Hariyanto	7	12	5	-	-	24
Herianto salim	-	5	-	6	6	17
dimas.wahyu	-	3	-	-	-	3

BUMA ID Team

#	Sprint
S1	Release 3.1.0 (Sprint 2)
S2	Release 4.0.0 - S1
S3	Release 4.0.0 - S2
S4	Release 4.0.0 - S3
S5	4.1.0 - Improve and Fix

Nama	S1	S2	S3	S4	S5	Total
Riki Ahmad Fadilah	36	26	33	48	23	166
Dian Heryana	32	13	31	26	25	127
nurrahman hadi	32	14	27	35	19	127
dimas.wahyu	19	5	18	26	14	82
v-darwin.samalo	5	-	1	13	-	19
Gita Riskayanti	-	-	-	13	5	18
Muhammad Zaqi Ghifari	3	-	-	13	-	16
Yvonne Priscilla	-	-	-	13	-	13
Muhammad Abdu Ar Rahman	9	-	-	-	-	9
Ivan Tri Wibowo	5	-	-	1	-	6
Devi Stephanie Sihombing	3	-	-	-	-	3
Ahmad Taufiq Hidayat	3	-	-	-	-	3
Varian Aditya Iryanto	-	-	-	-	2	2
